ID	WBS	Task Name	Duration	Start	Finish	Predecesso	Resource Names
1	**1**	**PHASE 1: INITIATION & SETUP**	4 days	**Thu 2/26/26**	**Tue 3/3/26**		
2	1.1	Project Handover: Sales to Production	1 day	Thu 2/26/26	Thu 2/26/26		Sales Mgr,Project Manager
3	1.2	Review Contract, Scope & Budget Specs	1 day	Fri 2/27/26	Fri 2/27/26	2	Project Manager
4	1.3	Technical Specification Revi	1 day	Mon 3/2/26	Mon 3/2/26	3	Eng Lead,Project Coordinator
5	1.4	Baseline Schedule Creation in MS Project	1 day	Tue 3/3/26	Tue 3/3/26	4	Project Coordinator
6	1.5	Milestone: Internal Project Kickoff	0 days	Tue 3/3/26	Tue 3/3/26	5	Project Manager,Project Coordinator,Eng Lead
7	**2**	**PHASE 2: ENGINEERING & DRAFTING**	7 days	**Wed 3/4/26**	**Thu 3/12/26**		
8	2.1	Approve Budget for Site Measurements	0.5 days	Wed 3/4/26	Wed 3/4/26	6	Project Manager
9	2.2	Field Technician Site Measurement (St.	1 day	Wed 3/4/26	Thu 3/5/26	8	Field Tech,Project Coordinator
10	2.3	Coordinate Electrical Rough-in Locations with	1 day	Thu 3/5/26	Fri 3/6/26	9	Project Coordinator
11	2.4	3D Modeling of Custom Desk Chassis	2 days	Thu 3/5/26	Mon 3/9/26	9	CAD Drafter
12	2.5	Draft 2D Production Shop Drawings	2 days	Mon 3/9/26	Wed 3/11/26	11	CAD Drafter
13	2.6	Develop Hardware & Lighting Schedule	1 day	Mon 3/9/26	Tue 3/10/26	11	Engineering,Project Coordinator
14	2.7	Internal Clash Detection & Structural Review	1.5 days	Wed 3/11/26	Thu 3/12/26	12,13	Eng Lead,Floor Mgr,Project Coordinator
15	**3**	**PHASE 3: SUBMITTALS & APPROVALS**	13 days	**Wed 3/4/26**	**Fri 3/20/26**		
16	3.1	Submit Shop Drawings to Client for Review	0 days	Thu 3/12/26	Thu 3/12/26	14	Project Manager
17	3.2	Prepare Custom Wood Finish "Strike-Off" Samples	2 days	Wed 3/4/26	Thu 3/5/26	6	Finishing Dept,Project Coordinator
18	3.3	Order Custom Leather Swatches from Vendor	1 day	Wed 3/4/26	Wed 3/4/26	6	Procurement
19	3.4	Receive Leather Swatches & Verify Spec	3 days	Thu 3/5/26	Mon 3/9/26	18	Receiving,Project Coordinator
20	3.5	Client Review Period: Drawings & Physical	5 days	Fri 3/13/26	Thu 3/19/26	16,17,19	Client,Project Manager
21	3.6	Process Client Redlines & Update CAD Files	1 day	Fri 3/20/26	Fri 3/20/26	20	CAD Drafter,Project Coordinator
22	3.7	Milestone: Final Client Sign-off (Contract Locked)	0 days	Fri 3/20/26	Fri 3/20/26	21	Client,Project Manager
23	**4**	**PHASE 4: PROCUREMENT & INVENTORY**	15 days	**Mon 3/23/26**	**Fri 4/10/26**		
24	4.1	Generate Master Bill of Materials (BOM)	1 day	Mon 3/23/26	Mon 3/23/26	22	Engineering

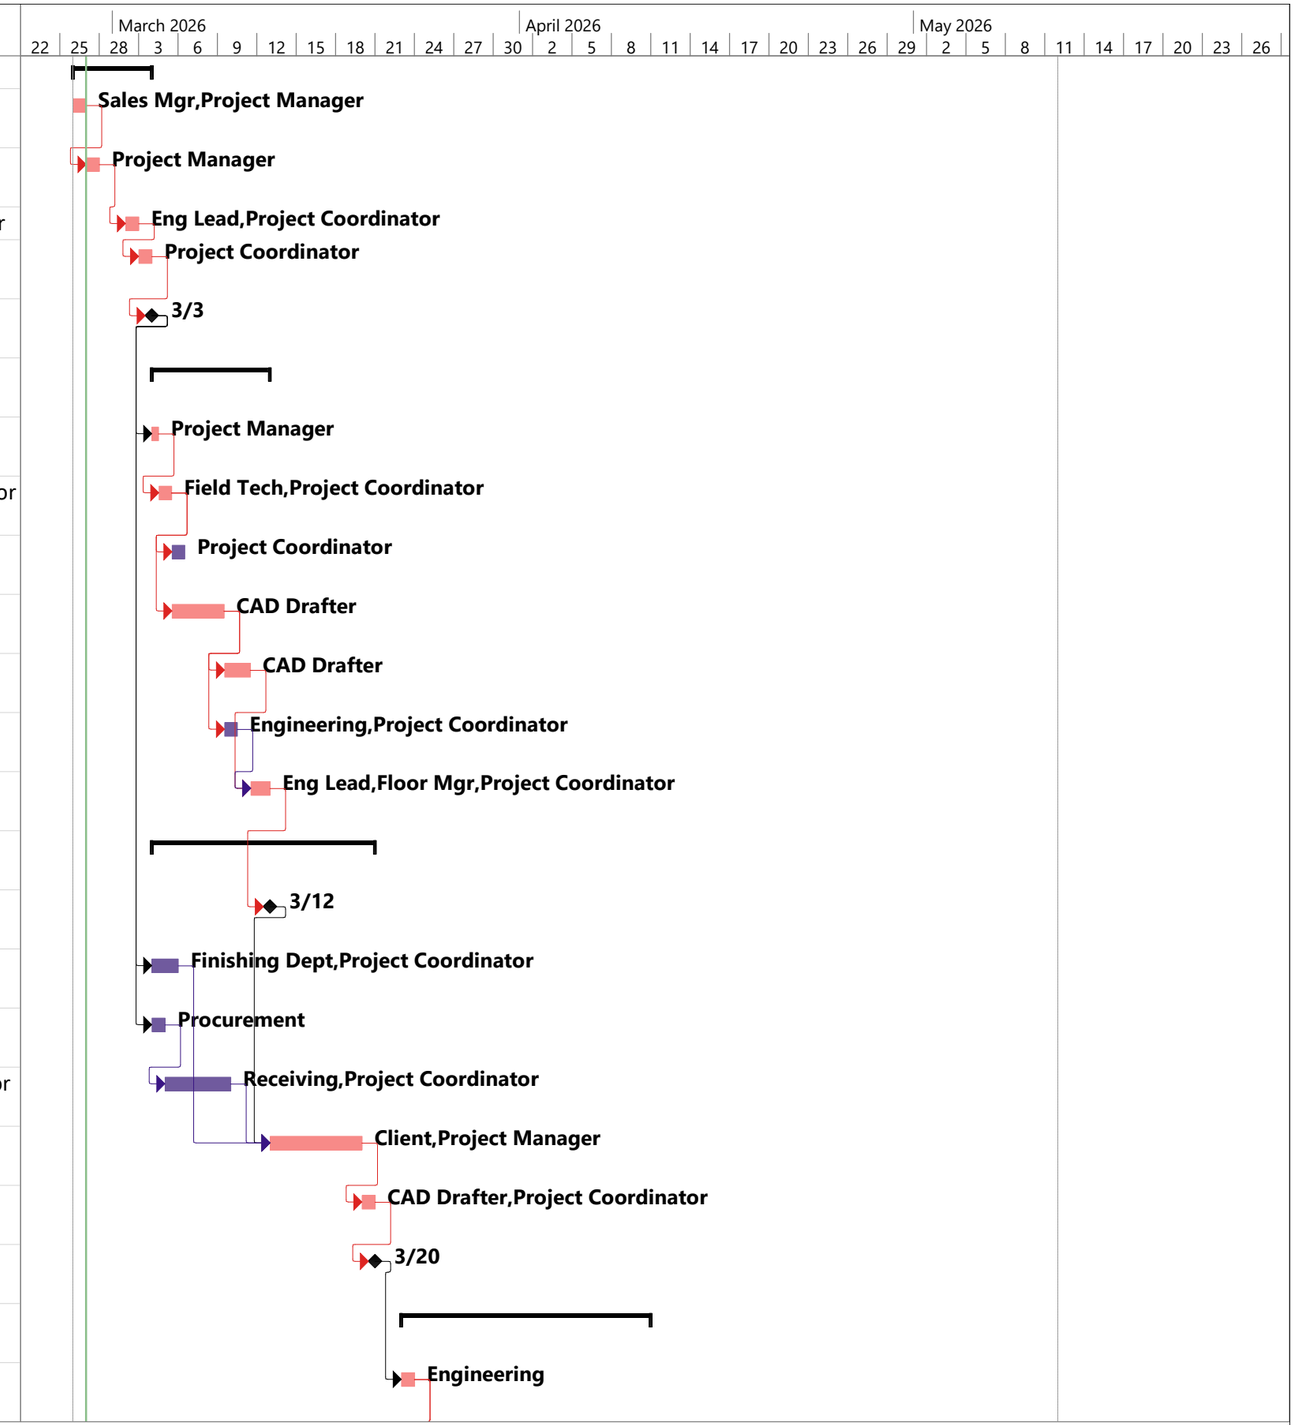

ID	WBS	Task Name	Duration	Start	Finish	Predecesso	Resource Names
25	4.2	PM Budget Approval for Specialty Materials	1 day	Tue 3/24/26	Tue 3/24/26	24	Project Manager
26	4.3	Issue POs: Sheet Goods (MDF) & Hardwoods	2.5 days	Wed 3/25/26	Fri 3/27/26	25	Procurement
27	4.4	Issue POs: Specialty Hardware & LED	1 day	Wed 3/25/26	Wed 3/25/26	25	Procurement
28	4.5	Issue PO: Custom Italian Leather Hides	1 day	Wed 3/25/26	Wed 3/25/26	25	Procurement
29	4.6	Track & Expedite Standard Materials	3 days	Fri 3/27/26	Wed 4/1/26	26,27	Project Coordinator
30	4.7	Receive Standard Materials (QA Check)	1 day	Wed 4/1/26	Thu 4/2/26	29	Receiving,Project Coordinator
31	4.8	Long Lead Transit: Custom Leather Hides	12 days	Thu 3/26/26	Fri 4/10/26	28	External Vendor
32	**5**	**PHASE 5: CNC MACHINING & MILLING**	11.5 days	**Tue 3/24/26**	**Wed 4/8/26**		
33	5.1	Generate CNC Machine Code (G-Code)	1 day	Tue 3/24/26	Tue 3/24/26	24	CNC Programmer
34	5.2	CNC Routing: Cut MDF/Plywood	2 days	Thu 4/2/26	Mon 4/6/26	30,33	CNC Operator
35	5.3	Mill Solid Hardwood Edges & Architectural Trims	1 day	Thu 4/2/26	Fri 4/3/26	30	Cabinetmaker
36	5.4	Apply PUR Edgebanding to Exposed Panels	1 day	Mon 4/6/26	Tue 4/7/26	34	Machine Operator
37	5.5	Bore Dowel Holes & Hardware Mounting Points	1 day	Tue 4/7/26	Wed 4/8/26	36	CNC Operator
38	**6**	**PHASE 6: SUB-ASSEMBLY & DRY FIT**	4.5 days	**Wed 4/8/26**	**Tue 4/14/26**		
39	6.1	Pre-Assembly Sort & BOM Verification	0.5 days	Wed 4/8/26	Wed 4/8/26	35,37	Assembly Team,Project Coordinator
40	6.2	Construct Internal Drawer B	1 day	Thu 4/9/26	Thu 4/9/26	39	Cabinetmaker
41	6.3	Glue, Dowel & Clamp Main Desk Carcass	2 days	Thu 4/9/26	Fri 4/10/26	39	Assembly Team
42	6.4	Route Channels for LED Lighting Strips	0.5 days	Mon 4/13/26	Mon 4/13/26	41	Cabinetmaker
43	6.5	Dry-Fit All Hardware (Slides, Hinges) & Remove	1 day	Mon 4/13/26	Tue 4/14/26	42	Cabinetmaker
44	6.6	QC Hold Point: Frame Squareness & Tolerance	0.5 days	Tue 4/14/26	Tue 4/14/26	43	Project Coordinator,Floor Mgr
45	**7**	**PHASE 7: FINISHING (CRITICAL PATH)**	12.5 days	**Wed 4/15/26**	**Fri 5/1/26**		
46	7.1	Final White-Wood Sanding & Putty Prep	1 day	Wed 4/15/26	Wed 4/15/26	44	Finishing Team
47	7.2	Apply Custom Base Stain to Client Spec	1 day	Thu 4/16/26	Thu 4/16/26	46	Finishing Dept
48	7.3	Apply Vinyl Wash-Coat / Sea	1 day	Fri 4/17/26	Fri 4/17/26	47	Finishing Dept
49	7.4	Lag Time: Sealer Curing Pro	1 day	Tue 4/21/26	Tue 4/21/26	48FS+1 da	

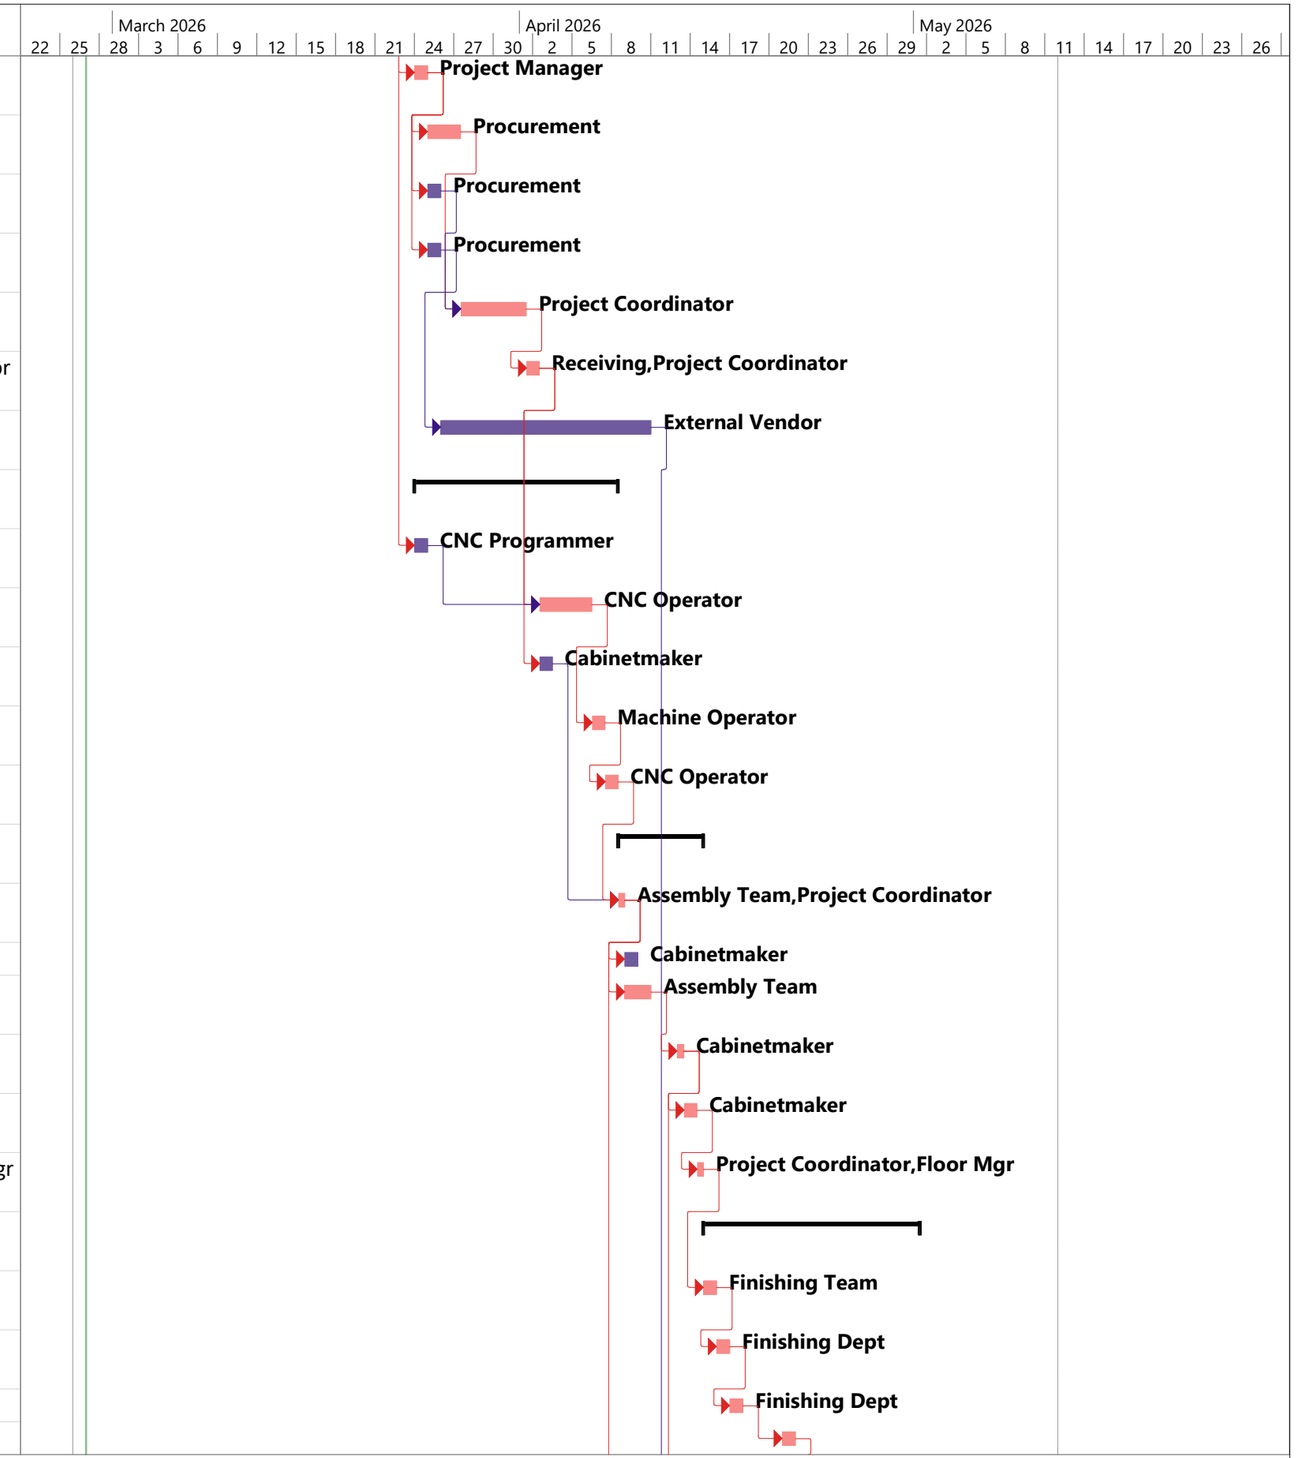

ID	WBS	Task Name	Duration	Start	Finish	Predecesso	Resource Names
50	7.5	Scuff Sanding of Sealer Coat	0.5 days	Wed 4/22/26	Wed 4/22/...	49	Finishing Team
51	7.6	Apply Commercial Conversion Varnish	0.5 days	Wed 4/22/26	Wed 4/22/26	50	Finishing Dept
52	7.7	Lag Time: Final Chemical Topcoat Cure	3 days	Tue 4/28/26	Thu 4/30/26	51FS+3 days	
53	7.8	QC Hold Point: Finish Consistency & Mil-Thickness Check	0.5 days	Fri 5/1/26	Fri 5/1/26	52	Project Coordinator,Finishing Mgr
54	**8**	**PHASE 8: UPHOLSTERY & ELECTRICAL**	4 days	**Thu 4/9/26**	**Tue 4/14/26**		
55	8.1	Expedite & Receive Custom Leather Hides	0.5 days	Mon 4/13/26	Mon 4/13/26	31	Project Coordinator
56	8.2	Cut High-Density Foam & Glue to Substrate	1 day	Thu 4/9/26	Thu 4/9/26	39	Upholstery Team
57	8.3	Cut, Sew, & Stretch Leather over Foam	1.5 days	Mon 4/13/26	Tue 4/14/26	55,56	Upholstery Team
58	8.4	Install LED Strips & Test Drivers (Pre-assembly)	1 day	Mon 4/13/26	Tue 4/14/26	42	Electrical Tech
59	**9**	**PHASE 9: FINAL INTEGRATION & QA**	3 days	**Fri 5/1/26**	**Wed 5/6/26**		
60	9.1	Re-install All Drawer Hardware & Tracks	1 day	Fri 5/1/26	Mon 5/4/26	53	Assembly Team
61	9.2	Mount Upholstered Leather Panels to Desk	0.5 days	Mon 5/4/26	Mon 5/4/26	57,60	Assembly Team
62	9.3	Final Assembly Check & Electrical Test	0.5 days	Tue 5/5/26	Tue 5/5/26	58,61	Cabinetmaker
63	9.4	Perform 99.8% Accuracy Specification Audit	0.5 days	Tue 5/5/26	Tue 5/5/26	62	Project Coordinator
64	9.5	PM Final Walkthrough & Client Photo Approval	0.5 days	Wed 5/6/26	Wed 5/6/26	63	Project Manager
65	**10**	**PHASE 10: PACKAGING & LOGISTICS**	2.5 days	**Wed 5/6/26**	**Fri 5/8/26**		
66	10.1	Verify Site Readiness (Flooring/Paint Complete) with GC	1 day	Wed 5/6/26	Thu 5/7/26	64	Project Coordinator
67	10.2	Construct Custom Wooden Shipping Crate	1 day	Wed 5/6/26	Thu 5/7/26	64	Shipping Team
68	10.3	Secure Desk into Crate & Wrap (White-Glove)	1 day	Thu 5/7/26	Fri 5/8/26	67	Shipping Team
69	10.4	Generate Shipping Manifest & Bill of Lading	0.5 days	Wed 5/6/26	Wed 5/6/26	63	Project Coordinator
70	10.5	Milestone: Desk Dispatched to Site	0 days	Fri 5/8/26	Fri 5/8/26	66,68,69	Logistics
71	10.6	Trigger Final Client Invoice	0 days	Fri 5/8/26	Fri 5/8/26	70	Project Manager
72	**11**	**PHASE 11: PROJECT CLOSURE**	1 day	**Fri 5/8/26**	**Mon 5/11...**		
73	11.1	Conduct Post-Mortem & Scrap Yield Analysis	1 day	Fri 5/8/26	Mon 5/11/26	70	Project Coordinator

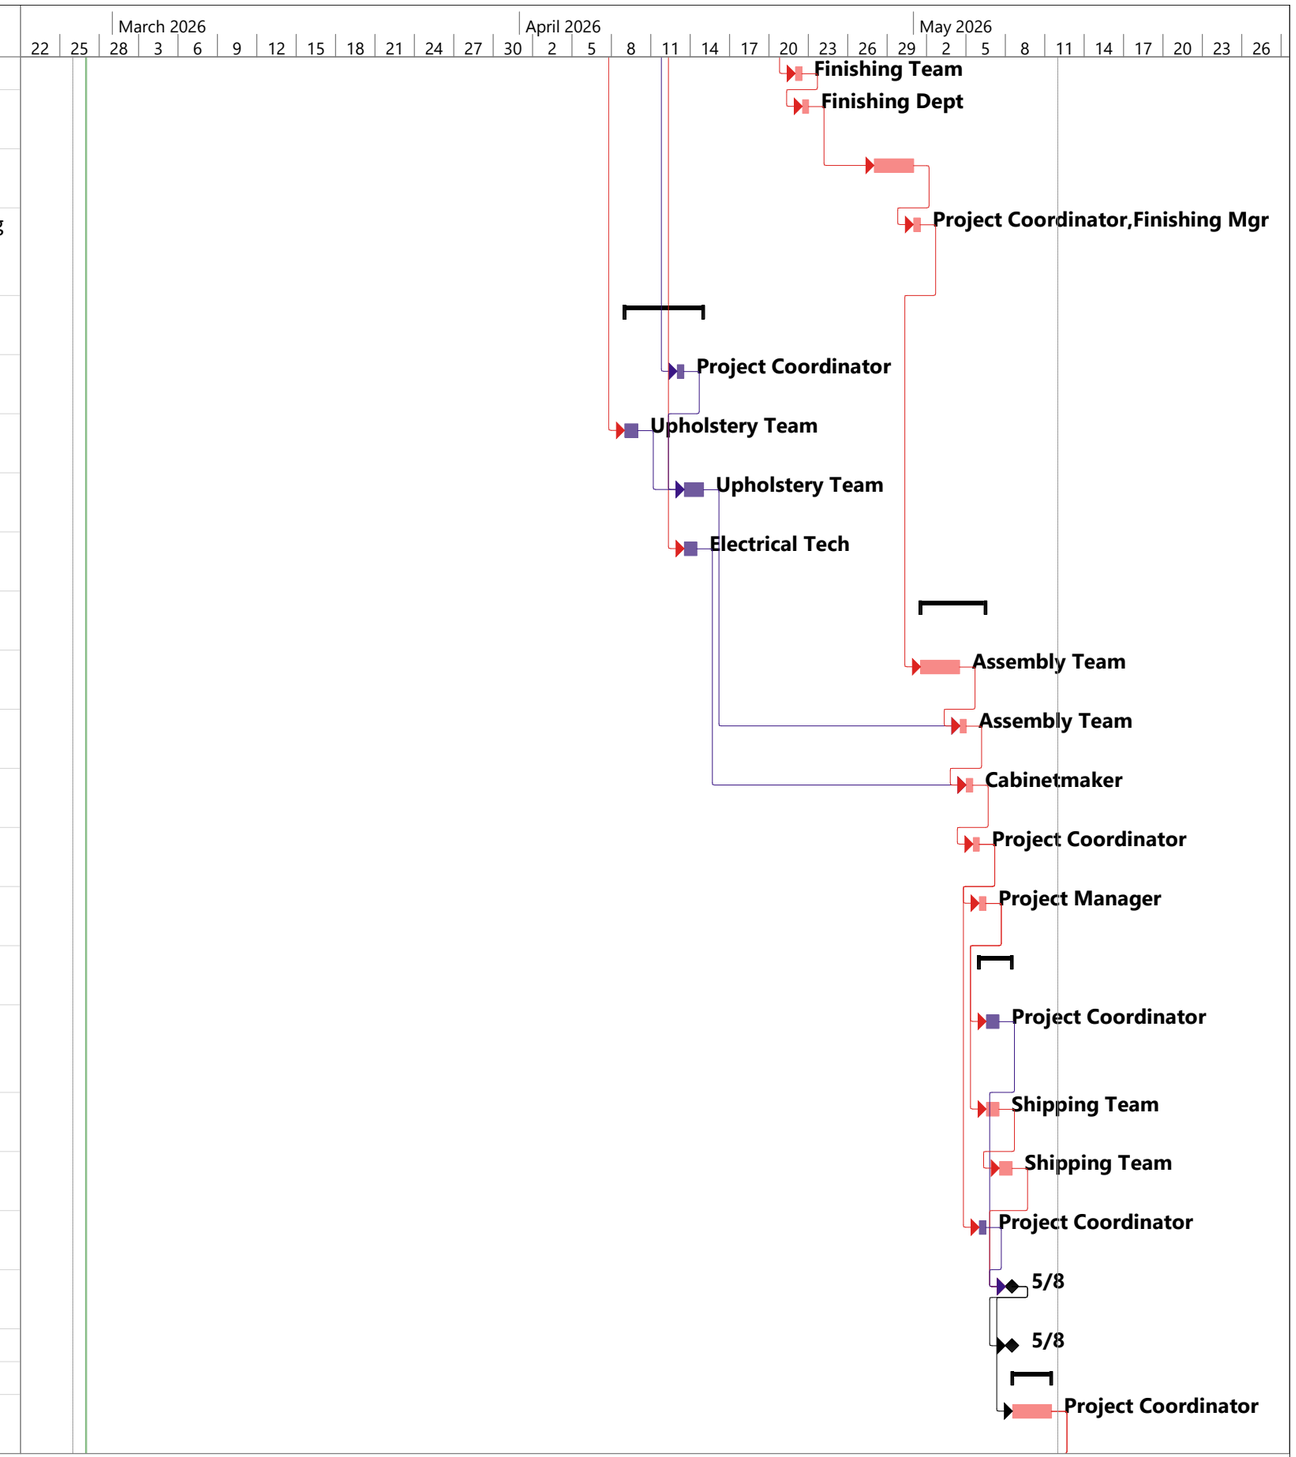

ID	WBS	Task Name	Duration	Start	Finish	Predecesso	Resource Names
74	11.2	Log Process Bottlenecks for Continuous Improvement	0 days	Mon 5/11/26	Mon 5/11/26	73	Project Coordinator,Eng Lead
75	11.3	Finalize As-Built Drawings & Handover Binder	0 days	Mon 5/11/26	Mon 5/11/26	73	Project Coordinator
